House Renovation Project

Product Backlog Items:

- 1. Paint the bedroom (Sprint 1)
- 2. Repair the main gate (Sprint 2)
- 3. Refurbish the kitchen area (Sprint 3)

Sprint 1


Sprint Backlog Item - Paint the bedroom

Task 1: Determine the activities needed to complete the chosen sprint backlog item(s)

Activities:


- 1. Purchase painting materials
 - 1.1 Survey and calculate costings
 - 1.2 Buy the materials
- 2. Prepare the site
 - 2.1 Clear the room
 - 2.2 Remove debris
- 3. Construct the room
 - 3.1 Repairing works
 - 3.2 Paint the ceiling
 - 3.3 Paint the walls
 - 3.4 Paint the door
- 4. Clean up the room
 - 4.1 Remove scrap and vacuum the room
 - 4.2 Move in the furniture

Task 2: Draw the Work Breakdown Structure (WBS) for Sprint 1

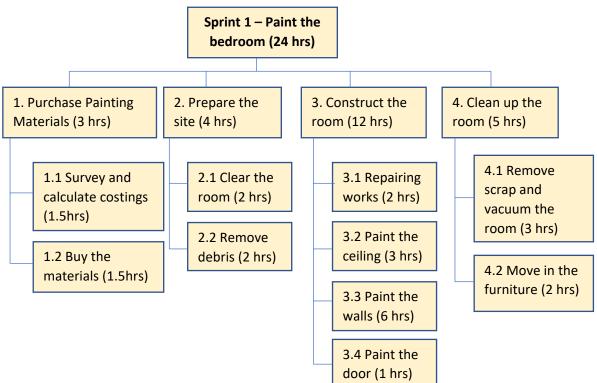

^{**} Each sprint will last for 3 days, working hours for each day is 8 hours

Task 3: Input the WBS into Trello Board

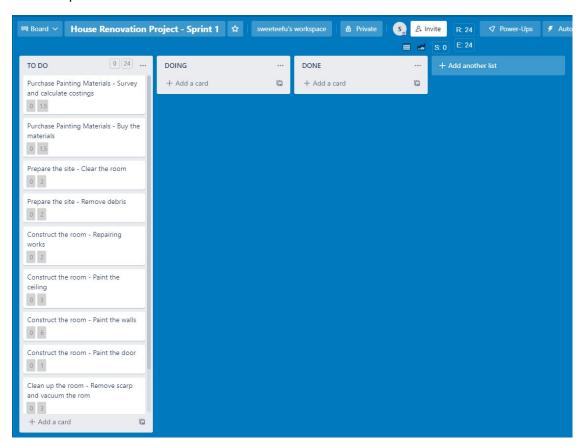

Task 4: Track the daily progress using Trello and burndownfortrello (https://www.burndownfortrello.com/)

